

KIEWIT SHEA TRAYLOR JOINT VENTURE

VTA's BART Silicon Valley Phase II Extension Project – Tunnel & Trackwork

PRE-BID MEETING **EARLY WORKS PACKAGES 3A**

DECEMBER 21, 2022

Agenda

Topic	Speaker
Welcome + Introductions	Abbigail Brown, CPM Logistics
Program/Project Overview <ul style="list-style-type: none">Schedule of Bids and ConstructionProject Requirements	Tom Trimble, KSTJV
Early Works Packages 3A <ul style="list-style-type: none">Location, ScheduleBid Opportunities/ScopesBuildingConnected	John Munsey, KSTJV Jaryd Frost, KSTJV
Resources and Assistance <ul style="list-style-type: none">KSTJV Technical Assistance: Module 1<ul style="list-style-type: none">Office SessionsDebrief Sessions	Abbigail Brown, CPM Logistics
Q&A	All

PROGRAM / PROJECT OVERVIEW

- BSV – Phase II Program Details
- CP 2 - Schedule
- CP 2 – Requirements

BSV – Phase II

- Largest public infrastructure program ever constructed in Santa Clara
- Includes the recently completed 10-mile, two-station Berryessa Extension Project (SVBX) and the Phase II Extension Project (BSVII Program)

For more information:

<http://www.vta.org/projects/bart-sv/phase-ii>



CP2 Overview

- **Scope:** Tunnel / Trackwork
- **Overall Estimated Budget:** \$2.5-3 Billion
- **Delivery Method:** Progressive Design-Build
- **Milestone Schedule:**
 - LNTP – June 9, 2022
 - Innovations Period
 - NTP1 – Sept. 8 2022
 - Stage 1 – Programming Services
 - **NTP1a – March 2023**
 - **Stage 1 – Design Work and Early Works**
 - NTP2 – June 2024
 - Stage 2 - Construction
 - CP2 Substantial Completion - 2029



Project Labor Agreement

- PLA with sub/contractors of all tiers from Santa Clara and San Benito Building & Construction Trades Council and its affiliated local Unions.
- Applies to VTA contracts of \$2 million and above
- Does not replace, interfere with, abrogate, diminish or modify existing local or national collective bargaining agreements in effect during Project duration.

DBE/SBE Participation

- **DBE: 15%**
Only DBE firms **certified by CUCP** will count toward DBE participation.
- **SBE: 20%**
Only SBE firms **certified by VTA or California DGS** will be counted for SBE participation.
- The 20% SBE goal is inclusive of the DBE goal, for this contract.

Owner-Controlled Insurance Program

- The sponsor of the insurance program will be the Santa Clara Valley Transportation Authority (VTA).
- Enrolled Participants will generally include all contractors and subcontractors of every tier involved with on-site project construction.

CP-2 Early Works Package 3A

- Location
- Scopes
- Schedule
- BuildingConnected

Early Works Package 3a: **Google Earth**



Santa Clara University

Coleman Ave.


San Jose Airport

CP2 - West Portal

Earthquakes Stadium

Highway 880

Early Works Package 3a: **Site Map**

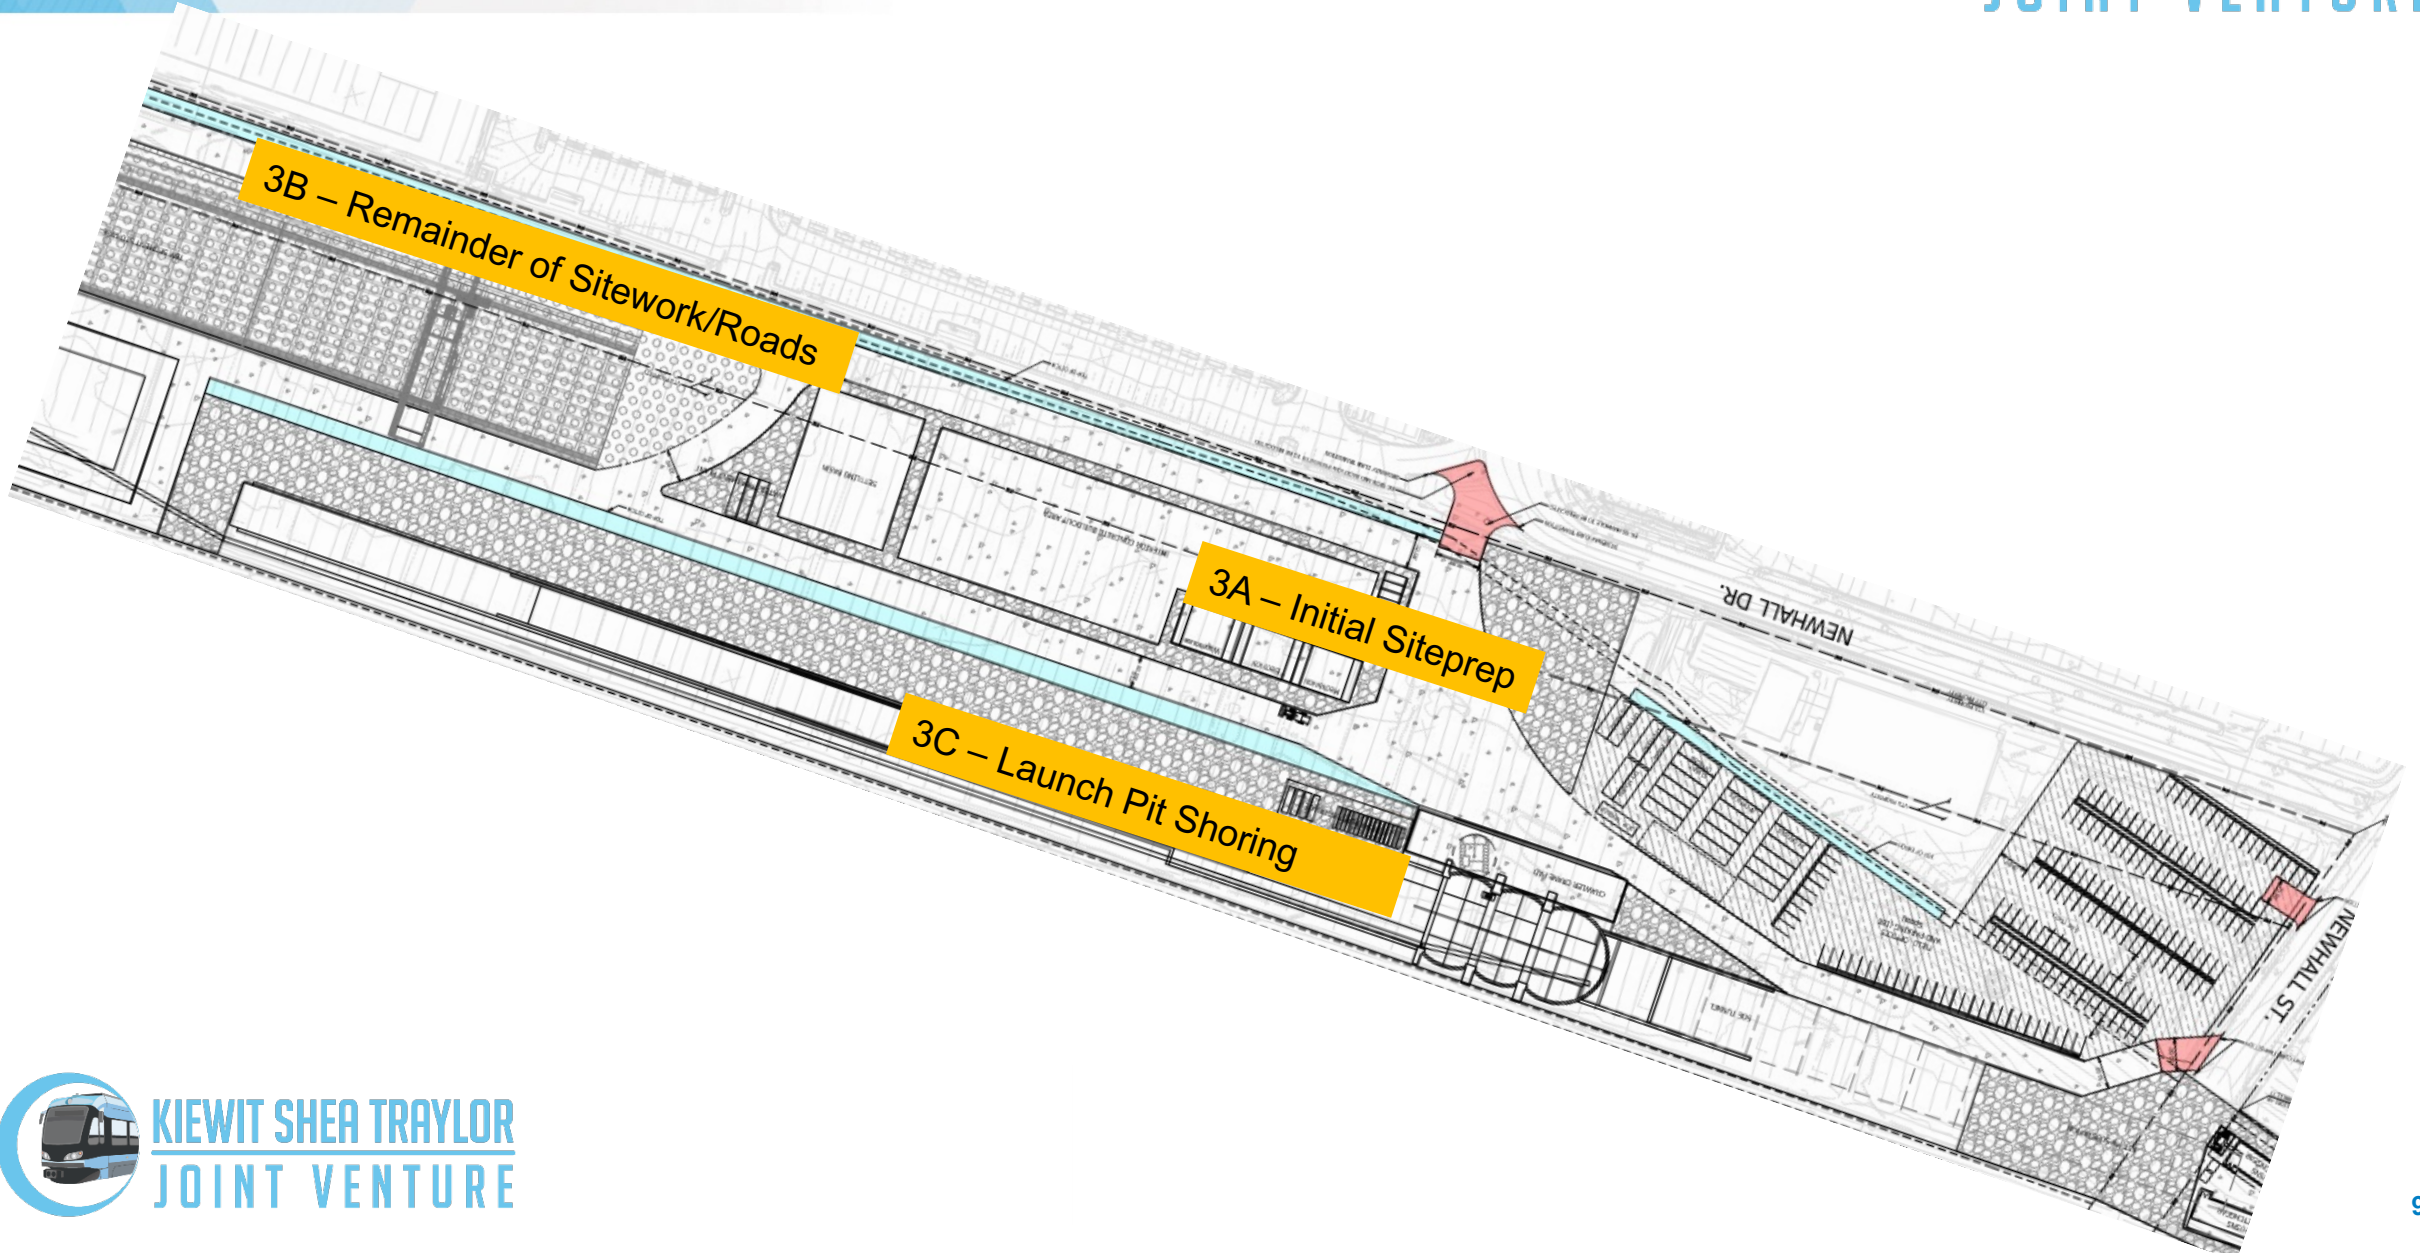

Early Works Package 3a: **Bid Packages**

- OSR Hourly Trucking
- Underground Utility Pip
- Aggregates (Buy & Haul)
- Erosion Control/BMP STS
- MOT Supplies (K-Rail)
- Street Sweeper Sub
- Sub Clean Out Existing Storm Drain (Newhall Yard)
- Tandem Axle Vac Truck
- Fencing Sub
- Wells Sub
- Trucking Sub
- AC Paving Sub
- Traffic Signs & Striping Sub
- Hydroseed Sub
- Wheel Wash Station
- 40 Yard Dumpster
- Sub - Security Guard
- PVC Pipe
- Sub - Site Prep - Lime Treat
- Office Trailer
- Water Treatment Sub

West Portal Site Preparation

Bid Advertisement Date: Week of Dec. 9, 2022

Bid Due Date: January 13, 2023

- Other early works packages will be advertised for solicitation in Q2 + Q3 of 2023.
- Register with [BuildingConnected](#) to receive bid notifications!
- **Indicate your scope of interest: BuildingConnected; KSTJV@Kiewit.com**
- **Submit Bids: BuildingConnected**
- Visit KSTJV.com for more project information.

BUILDINGCONNECTED Increase your win rate by up to 25% with Bid Board Pro [CHECK IT OUT](#)

JF Bid Board

- Undecided 2
- Accepted 0
- Submitted 2
- Won 0

CP2 - BART Silicon Valley Phase II (BSVII) Tunnel / Trackwork...
Early Works Package 3a

Overview Files Messages Bid Form

Opportunity Summary ✓ Bidding

Register with BuildingConnected to:

- Receive bid notifications
- Indicate your scope of interest
- Submit Bids

Connect with Us

Bidder's List + Planroom

- Create an account with [BuildingConnected](#)
- Bid solicitations and vendor communications regarding plans/specs/addenda distribution.

Subcontractor Questionnaire

- Help us understand your capabilities and bidding interest for this project.
- KSTJV.com

VTA BART Silicon Valley Phase II Extension - Contract No. 2 Tunnel/Trackwork

Subcontractor Questionnaire

Contact First Name *

Contact Last Name *

Company Name *

Email Address *

Phone Number *

Address *

Website / URL *

Type of Work (Prof. Svcs, Const. Supplier) *

Professional Services Construction Vendor/Supplier

Please indicate the NAICS codes/services your company performs: *

Firm Description *

Please attach capability statement, if available:

Drag and drop files here or [browse files](#)

How many employees does your organization have?

Resources + Assistance

- Technical Assistant Program
- Module 1: Bid Submittal Assistance (BSA)

Stay Informed: www.KSTJV.com

**KIEWIT SHEA TRAYLOR
JOINT VENTURE**

- Project Information
- Contract Opportunities
- Subcontractor/Database sign-up
- Events Calendar
- Resource List
- Virtual Technical Assistance Hub
- Materials from past workshops:
 - Progressive Design Build
 - Understanding Project Reqs.
 - Navigating BuildingConnected
 - Getting Certified

www.kstjv.com



Resources

KSTJV is committed to providing resources, information, and support to local, small, and diverse business opportunities to participate on the Project.

ARE YOU ON TRACK FOR OPPORTUNITY?
CLICK HERE TO VISIT OUR ASSISTANCE HUB FOR RESOURCES AND ASSISTANCE

VTA BART Silicon Valley Phase II Extension Program

The Santa Clara Valley Transportation Authority's (VTA) BART Silicon Valley Extension Program (BSV Program) is the largest public infrastructure Program ever constructed in Santa Clara County, California. The Program includes the recently completed 10-mile, two-station Berryessa Extension Project (SVBX) and the Phase II Extension Project (BSVII Program).

The BSVII Program will extend Bay Area Rapid Transit (BART) service from the existing temporary end of the SVBX line adjacent to the Berryessa/North San Jose BART station through downtown San Jose, terminating in the City of Santa Clara.

ACCOUNTING

ALTERNATIVE DELIVERY

BONDING

BUSINESS DEVELOPMENT

CERTIFICATION

CONTRACTS/RISK ASSESSMENT

COVID-19

ESTIMATING

HR BEST PRACTICES

INSURANCE

OCIP

PREVAILING WAGE

PROJECT LABOR AGREEMENTS

QUALITY

RISK MANAGEMENT

SAFETY

TEAMING

Technical Assistance Program

Module 1

Bid Submittal Assistance (BSA)

- Ready firms with relevant scope and capacity for submitting viable bids on scope packages being advertised.
- Concurrent with bid solicitations process

Module 2

Mentor-Protégé Program (MPP)


- Create and support individualized learning plan focused on self-selected barriers.

Module 3

Collective Group Mentoring (CGM)

- Build capacity within contracting community to engage on public works projects through a collective mentoring approach.

Bid Submittal Assistance (BSA)

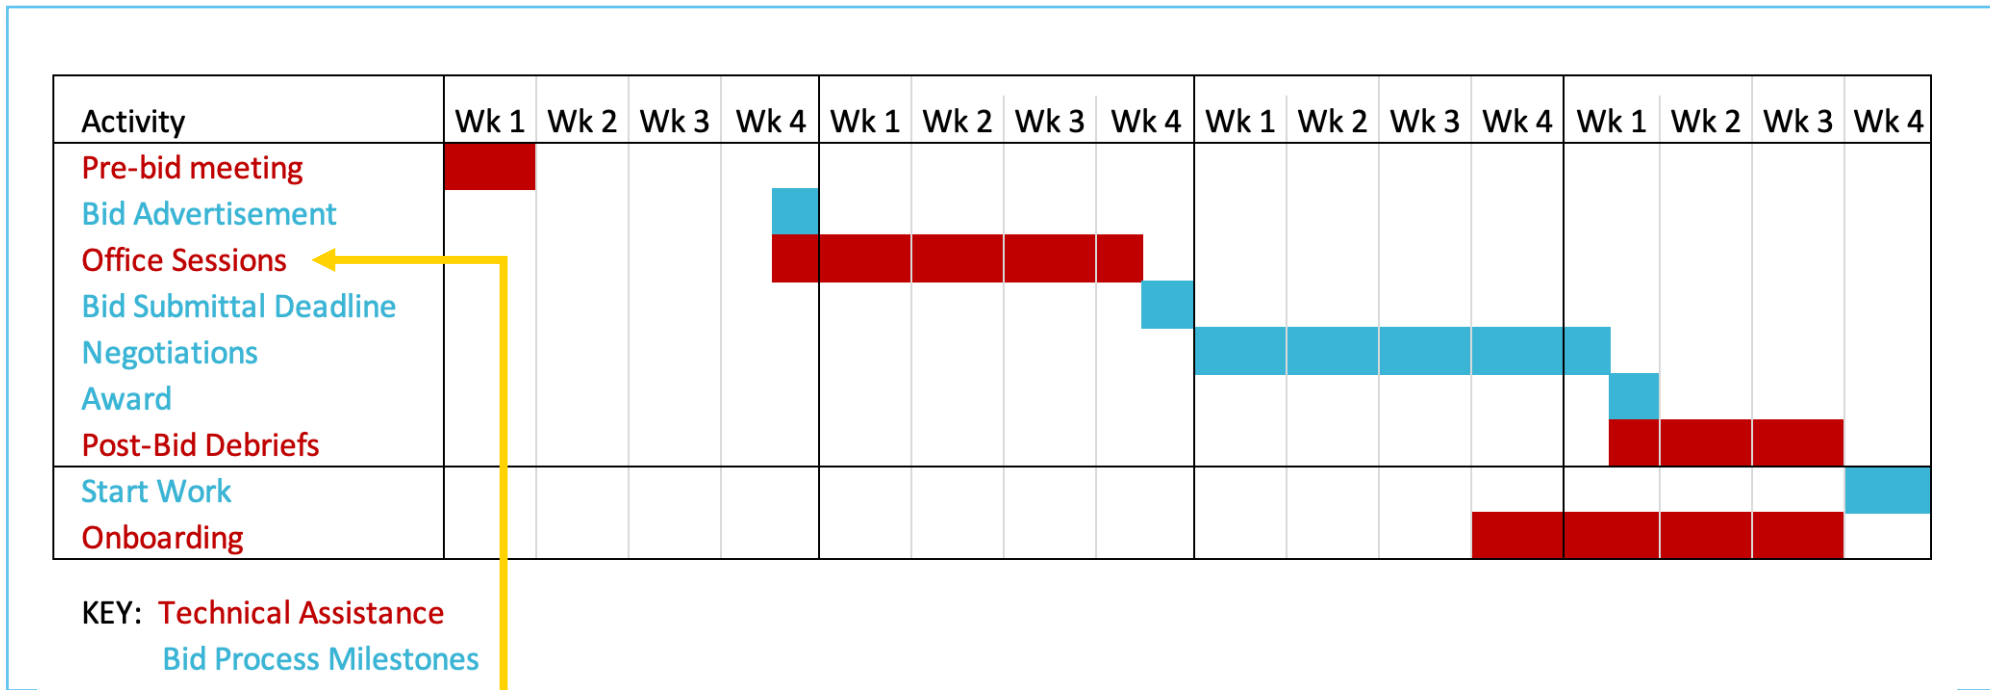

CP2 EWP 3A OFFICE SESSIONS

DATE: Friday, January 6, 2023
 TIME: 10:00 am to 12:00 pm
 ONLINE: Zoom

SIGN UP TODAY!



bit.ly/3WtKkFK



KIEWIT SHEA TRAYLOR

JOINT VENTURE

**Thank you for
joining us!**

**Do you have any
questions?**
